### March 2020

# 👔 King County

Operational performance metrics

The King County Wastewater Treatment Division (WTD) provides relevant information on operational, financial, regulatory and safety performance of the utility. Much of this information is updated monthly.

#### This information:

- Shares an overview of the system
- Presents operational patterns
- Illustrates system dynamics
- Identifies approaching challenges

### **Operational metrics**

The following metrics represent the performance of the King County Wastewater Treatment Division in four key performance areas:


- Operational performance
- Regulatory performance
- Financial performance
- Safety performance

### **Operational performance (March 2020)**

### 1. Flow volumes at regional plants and key points in the system

### Flow volumes at regional plants and key points in the system

The following graphs illustrate the total amount of flow to each of our regional treatment plants over various periods of time including flows through the Combined Sewer Overflow system. The bars at the bottom of the first graph illustrate the impact that rainfall has on our system.

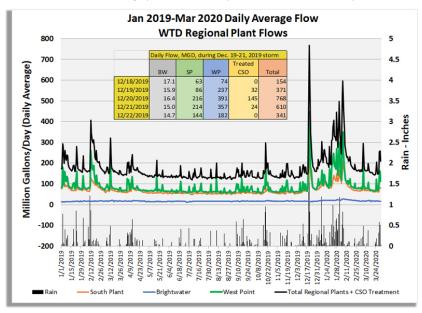


### Contact us

If you have questions regarding this information, please contact:


Olivia Robinson at Olivia.Robinson@kingcounty.gov


| 206-477-3566 |  |
|--------------|--|
|              |  |




+

March 2020

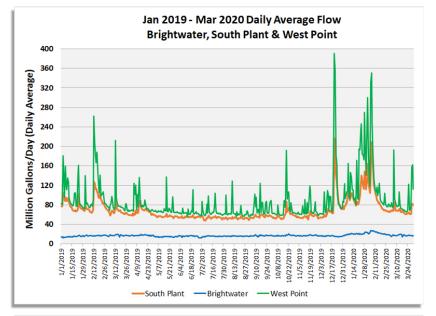

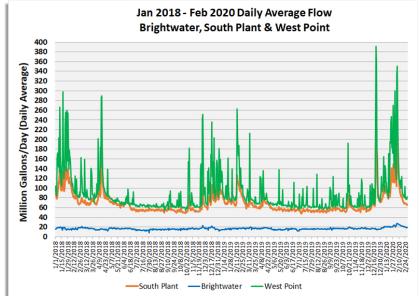


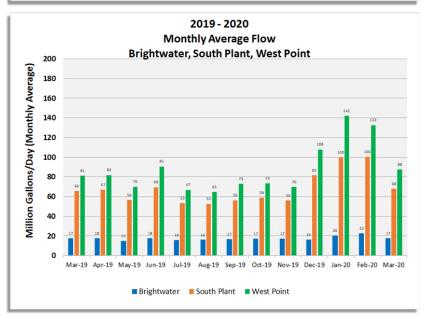

March 2020

+


+

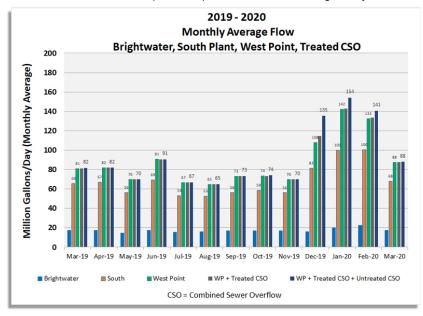

### 2. Combined Sewer Overflow (CSO) discharge volumes throughout the system

### Combined Sewer Overflow (CSO) discharge volumes throughout the system

The following graph illustrates the total amount of flow that is handled through the regional Combined Sewer Overflow system. Here is the link that shows our CSO locations: https://www.kingcounty.gov/services/environment/wastewater/cso/library/map.aspx

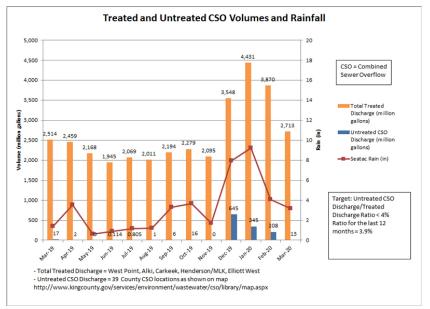



### 3. Production and distribution of Loop biosolids

### Production and distribution of Loop biosolids

Biosolids are the nutrient-rich product of the wastewater treatment process. Biosolids improve soil fertility and enhance plant growth and crop yield. Loop® is the brand name for biosolids produced by King County. Loop is used as fertilizer and soil amendment for commercial forestry and agriculture, and as an ingredient in compost for landscaping and home gardening.

King County's biosolids program is responsible for managing Loop recycling, including transportation and delivery, permitting and managing Loop applications, research and monitoring, and public outreach. Since 1973, we have worked with local organizations, farm groups, and university scientists to develop an award-winning program that serves as a model for safe, sustainable biosolids recycling.

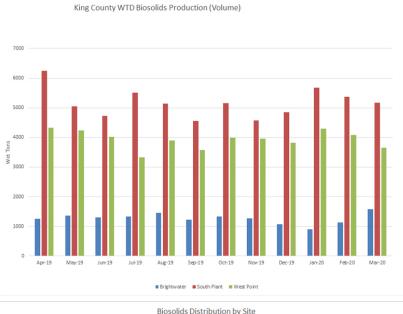

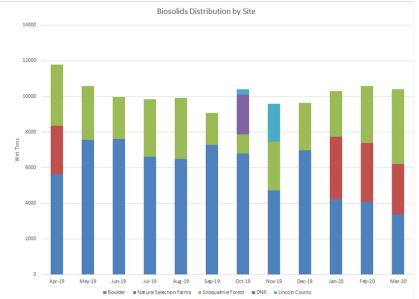


### 4. Electrical energy usage at each regional treatment plant and conveyance system +

### Electrical energy usage at each regional treatment plant and conveyance system

### Monthly Average Electricity Use at Brightwater, South Plant and West Point:


This diagram shows the average daily electricity use for the past 13 months for each of King County's three main treatment plants. West Point's electricity use depends mainly on treated volume. South Plant's electricity use is driven by influent flow and oxygen demand for nitrification. Brightwater's energy use is higher per gallon treated because of its elevated location, which requires more pumping, higher treatment standards, and stringent odor control requirements.




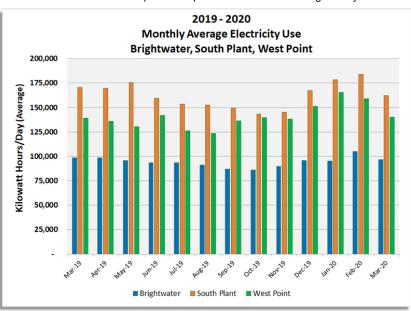

### Electricity Use at Brightwater, South Plant and West Point:

This diagram shows daily electricity use for each treatment plant. It highlights how electricity use can double with high flow volumes at West Point.

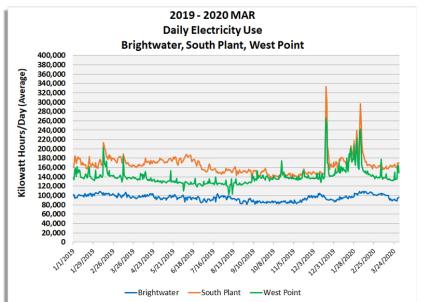


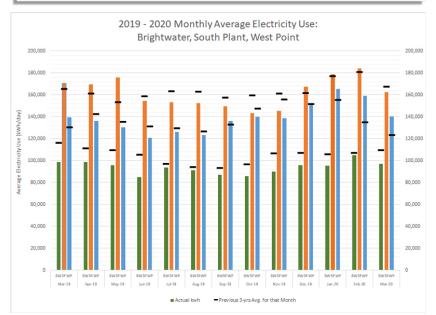

### Total WTD Offsite Energy Use

This diagram shows the combined energy use of WTD's more than one hundred offsite facilities. Energy use at offsite facilities is driven by flow volumes and outside air temperatures.


Please note: This information is updated monthly and will have a three-month lag when all of the data becomes available.

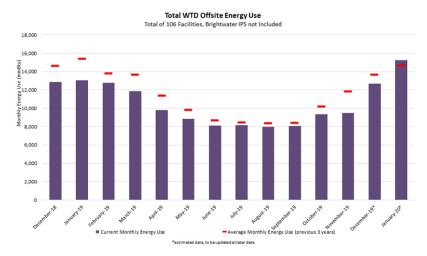

### Tracking WTD's progress towards its 7.5% energy reduction goal.

Normalized electricity use describes the amount of electricity a facility would have used if the general conditions had been the same as they were in the baseline year (2014). Normalizing energy use allows us to track changes in energy use independent of factors we do not control such as air temperatures or flow volumes. This diagram shows the change in normalized electricity use for each treatment plant, offsite facilities and WTD in total and how these changes compare to the County wide 2020 energy reduction goal.

**Please note:** This normalized electricity use information is updated once a quarter with a lag time of about three months.



+

## 5. Production and usage of biogas


### Production and usage of biogas

### WTD, Biogas Utilization

Biogas is used differently at each of the three treatment plants.

- At South Plant excess biogas can be fed into PSE's natural gas pipeline.
- At Brightwater and West Point biogas usage is limited to the equipment on site. At both of
  these plants there is a higher demand for biogas in winter when flows are higher and
  temperatures lower. The total amount of biogas beneficially used therefore tends to be
  higher in winter than in summer.

#### WTD, Biogas Utilization



### **Regulatory performance (March 2020)**

### 6. Significant power disruption events

### Significant power disruption events

The following table conveys information on the performance of the County's wastewater treatment facilities and conveyance system for any monthly exceedances of permit requirements that are caused by power disruption, or involve events with backups of the conveyance system and need for substantial responsive actions (e.g., cleanup of sanitary sewer overflows).

| E Hite -  |               |             |          |           | 2019      |          |           |         |     | 2020 |     |      |  |  |
|---|---------------|-------------|----------|-----------|-----------|----------|-----------|---------|-----|------|-----|------|--|--|
| Facility  | Apr           | May         | Jun      | Jul       | Aug       | Sep      | Oct       | Nov     | Dec | Jan  | Feb | Mar  |  |  |
| Wastewater Treatment I  | Plants (e     | e.g., efflu | uent lin | it exce   | edance,   | unpern   | nitted di | scharge | es) |      |     |      |  |  |
| West Point  |               |             |          | a         |           | b        |           | Ь       |     |      |     |      |  |  |
| South Plant   |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Brightwater   |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Vashon  |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Carnation   |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| CSO Treatment Facilities  | (e.g., ej     | ffluent li  | mit exc  | eedanc    | e, disinf | ection f | ailure)   |         |     |      |     |      |  |  |
| Henderson/MLK CSO   | *             | *           | *        | *         | *         | *        | *         | *       |     | *    |     | *    |  |  |
| Alki CSO  | *             | *           | *        | *         | *         | *        | *         | *       |     |      |     | *    |  |  |
| Carkeek CSO   | *             | *           | *        | *         | *         | *        | *         | *       |     |      |     | *    |  |  |
| Elliott West CSO  | *             | *           | *        | *         | *         | *        | *         | *       |     |      |     | *    |  |  |
| West Section Conveyance System  |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| CSO Exacerbated   |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Overflow  | flow          |             |          |           |           |          |           |         |     |      |     |      |  |  |
| CSO Dry Weather   | ) Dry Weather |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Overflow  |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Sanitary Sewer Overflow   |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| East Section Conveyance   | System        |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Sanitary Sewer Overflow   |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| Notes:  |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| 1         Number of power disruption/backup events in any month where exceedances occur.           Represents any month where no events occurred, or if any non-compliance occurred it was unrelated to power disruption, or backups in the conveyance system.           Non-compliance occurred and involved power disruption or conveyance system backup; however, repair/solution is known and the incident response and correction was immediate.           Non-compliance involving power disruption or conveyance system backup, and evaluation and corrective action includes substantial effects on residents and businesses, level of effort and time to resolve, or costs to system operations. |               |             |          |           |           |          |           |         |     |      |     |      |  |  |
| <ul> <li>Monitoring perio<br/>not operate with</li> <li>a A disturbance in the</li> </ul>   | a discha      | arge to t   | he outfa | all at an | y time i  | n the m  | onth.     |         |     |      |     | lion |  |  |

from flooding and normal operations were restored 27 min. after the bypass began.
 Temporary power disruptions at West Point on 12/20/18, 3/17/19, 9/7/19, and 11/15/19 resulted in brief secondary diversion events (i.e., blending of primary and secondary treated effluent); however, these diversions receive chlorine disinfection and no effluent limitations are exceeded.

### 7. Significant system process disruptions

+

+

Significant system process disruptions


The following table conveys information on the performance of the County's wastewater treatment facilities and conveyance system for any monthly exceedances of permit requirements that are caused by, or involve, process disruption (not power related) such as major equipment

+

or biological treatment process failures, or industrial discharges.

| Wastewater Treatment and Conveyance System Compliance Events - |                                     |           |          |          |            |          |          |          |      |     |     |     |
|--|-------------------------------------|-----------|----------|----------|------------|----------|----------|----------|------|-----|-----|-----|
| Permit Requirement Exceedances Involving Process Disruption    |                                     |           |          |          |            |          |          |          |      |     |     |     |
| Fo alling  |                                     |           |          | 2020     |            |          |          |          |      |     |     |     |
| Facility   | Apr May Jun Jul Aug Sep Oct Nov Dec |           |          |          |            |          |          |          |      | Jan | Feb | Mar |
| Wastewater Treatment P   | lants (e                            | .g., effl | ient lim | it excee | dance,     | unpern   | nitted a | lischarg | les) |     |     |     |
| West Point   |                                     |           |          |          |            |          |          |          |      |     |     |     |
| South Plant  |                                     |           |          |          |            |          |          |          |      |     |     |     |
| Brightwater  |                                     |           |          |          |            |          |          |          |      |     |     |     |
| Vashon   |                                     |           |          |          |            |          |          |          |      |     |     |     |
| Carnation  |                                     |           |          |          |            |          |          |          |      |     |     |     |
| CSO Treatment Facilities                                       | e.g., ef                            | fluent li | mit exce | edance   | e, disinfe | ection f | ailure)  |          |      |     |     |     |
| Henderson/MLK CSO  | *                                   | *         | *        | *        | *          | *        | *        | *        |      | *   | *   | *   |
| Alki CSO   | *                                   | *         | *        | *        | *          | *        | *        | *        | a    |     |     | *   |
| Carkeek CSO  | *                                   | *         | *        | *        | *          | *        | *        | *        |      |     | *   | *   |
| Elliott West CSO   | *                                   | *         | *        | *        | *          | *        | *        | *        | b    | b   | b   | *   |
| West Section Conveyance System                                 |                                     |           |          |          |            |          |          |          |      |     |     |     |
| Unpermitted Overflows  |                                     |           |          |          |            |          |          |          |      |     |     |     |
| East Section Conveyance  | System                              |           |          |          |            |          |          |          |      |     |     |     |
| Sanitary Sewer Overflow  |                                     |           |          |          |            |          |          |          |      |     |     |     |

Notes:



Non-compliance occurred and involved process disruption; however, repair/solution is known and the incident response and correction was immediate.

Non-compliance involving process disruption, and evaluation and corrective action includes substantial effects on residents and businesses, level of effort and time to resolve, or costs to system operations. Monitoring period characterized by sufficiently low flow conditions that the CSO treatment facility did

- Monitoring period characterized by sufficiently low flow conditions th not operate with a discharge to the outfall at any time in the month.
- The annual average total suspended solids removal limit was exceeded at Alki in 2018 and 2019.
   Performance evaluation of recent pumping control upgrades and optimization at the pump station and treatment operations is underway.
- b Effluent limit exceedances at Elliott West associated with process control performance; a phased planning and facility improvements process is underway.

#### 8. Regulatory compliance and performance

### Regulatory compliance and performance

The following table conveys information on the performance of King County's wastewater treatment facilities and conveyance system for any monthly exceedances of permit requirements that involve compliance with effluent limitations at the County's five wastewater treatment plants or four CSO treatment facilities, or unpermitted overflow events in the separated sanitary or combined stormwater-sewer conveyance system.

### March 2020

+

| NPDES Perm  | NPDES Permit Exceedances (Reportable Events Subject to Potential Penalties) – |          |        |         |        |         |     |     |     |     |      |     |
|---|---|----------|--------|---------|--------|---------|-----|-----|-----|-----|------|-----|
| 1   | Wastewater Treatment Facilities or Conveyance System                          |          |        |         |        |         |     |     |     |     |      |     |
| E - allite a  |   |          |        |         | 2019   |         |     |     |     |     | 2020 |     |
| Facility  | Apr   | May      | Jun    | Jul     | Aug    | Sep     | Oct | Nov | Dec | Jan | Feb  | Mar |
| Effluent Limitations Exceedances at Wastewater Treatment Facilities |   |          |        |         |        |         |     |     |     |     |      |     |
| West Point  |   |          |        | a       |        |         |     |     |     |     |      |     |
| South Plant   |   |          |        | b       |        |         |     |     |     |     |      |     |
| Brightwater   |   |          |        |         |        |         |     |     |     |     |      |     |
| Vashon  |   |          |        |         |        |         |     |     |     |     |      |     |
| Carnation   |   |          |        |         |        |         |     |     |     |     |      |     |
| Effluent Limitations Exceedances at CSO Treatment Facilities        |   |          |        |         |        |         |     |     |     |     |      |     |
| Henderson/MLK CSO   | *   | *        | *      | *       | *      | *       | *   | *   |     | *   | *    | *   |
| Alki CSO  | *   | *        | *      | *       | *      | *       | *   | *   | с   |     |      | *   |
| Carkeek CSO   | *   | *        | *      | *       | *      | *       | *   | *   |     |     | *    | *   |
| Elliott West CSO  | *   | *        | *      | *       | *      | *       | *   | *   | d   | d   | d    | *   |
| Conveyance System Over  | flow Eve  | nts in C | ombine | d or Se | parate | d Basin | 5   |     |     |     |      |     |
| West Section – Dry  |   |          |        |         |        |         |     |     |     |     |      |     |
| Weather Overflows at  |   |          |        |         |        |         |     |     |     |     |      |     |
| CSO Outfalls  |   |          |        |         |        |         |     |     |     |     |      |     |
| West Section – Sanitary   |   |          |        |         |        |         |     |     |     |     |      |     |
| Sewer Overflows   |   |          |        |         |        |         |     |     |     |     |      |     |
| East Section – Sanitary   |   |          |        |         |        |         |     |     |     |     |      |     |
| Sewer Overflows   |   |          |        |         |        |         |     |     |     |     |      |     |
| Notes:  |   |          |        |         |        |         |     |     |     |     |      |     |

Compliance goal for all events is "zero", and all exceedances have potential to be assessed penalties.

No ongoing non-compliance; or events with known cause and immediate correction. Ongoing compliance issue; but repairs/solution is known and underway for timely correction. \*

Substantial ongoing compliance issue with ongoing corrective actions, or response and/or planning for corrective action is underway. Monitoring period characterized by sufficiently low flow conditions that the CSO treatment

facility did not operate with a discharge to the outfall at any time in the month.

- A disturbance in the power supply to West Point on July 19th resulted in an emergency bypass of 2.1 million a gallons of untreated wastewater to Puget Sound. The systems operated as planned to protect the facility from flooding and normal operations were restored 27 min, after the bypass began.
- h A temporary loss of disinfection occurred at South Plant on July 18th during an equipment upgrade installation procedure that resulted in non-disinfected discharge to Puget Sound lasting about 79 min
- The annual average total suspended solids removal limit was exceeded at Alki in 2018 and 2019. Performance evaluation of recent pumping control upgrades and optimization at the pump station is underway.
- d A phased planning and facility improvements process is underway for Elliott West.

### 9. Water quality monitoring

#### Water quality monitoring

King County WTD conducts routine effluent water quality monitoring for compliance with the NPDES permit requirements at the County's five wastewater treatment plants, and at the four CSO treatment facilities. Additionally, WTD (in conjunction with scientists in King County Water and Land Resources Division [WLRD]) conducts specific sediment and water quality monitoring studies required for compliance with the NPDES permit as well as the Post Construction Monitoring Program for the County's 2012 Long-term CSO Control Plan Amendment. The following sections further describe these monitoring programs and provide information on the status of currently available monitoring efforts and data reports.

### Effluent Monitoring Data

WTD monitors treated wastewater (effluent) at each of the five main treatment plants (West Point, South Plant, Brightwater, Vashon, and Carnation) for a variety of conventional chemical and biological water quality properties which are used to track performance of the physical and biological treatment processes, and to ensure compliance with effluent limitations that are specified in the NPDES permit for the purposes of protecting the aquatic environment where the wastewater is discharged. WTD also conducts required effluent monitoring at the four CSO treatment facilities (Carkeek, Elliott West, Alki, and Henderson/Martin Luther King [H/MLK]) whenever wet weather storm events result in these facilities operating and discharging to their designated CSO outfalls. The majority of the routine effluent data that is collected to comply with applicable NDPES permit requirements is compiled and submitted to Ecology electronically as Discharge Monitoring Reports (DMRs) on a regular monthly basis.

The key parameters that are monitored for NPDES permit compliance with effluent limitations consist of biochemical oxygen demand (BOD), total suspended solids (TSS), settleable solids, pH, chlorine residual, and fecal coliform bacterial. The compliance with the effluent limitations is a primary method used by Ecology and WTD of evaluating routine and ongoing performance of the treatment processes. Accordingly, the reader is directed to review information presented above under "#8 -Regulatory Compliance and Performance" which provides a simplified summary of monthly plant performance that incorporates and interprets the diverse set of effluent monitoring data and information on any significant non-compliance events.

The effluent monitoring data and reports submitted to Ecology in monthly DMRs address many additional parameters that are not necessarily directly attributable to treatment process performance or NPDES regulatory compliance. However, the following attached files are the cover letters submitted for the most recent DMRs for each of the five wastewater treatment plants. The cover letters characterize each facility during the monitoring period including such items as flows,

March 2020

compliance with NPDES permit requirements, and any other important process performance events, news, or significant events. The facility DMR cover letters for the most recent monthly monitoring period follow:

- <u>Brightwater</u> (Permit No. WA0032247)
- <u>Carnation (Permit No. WA0032182</u>)
- South Plant △ (Permit No. WA0029581)
   Vashon △ (Permit No. WA0022527)
- <u>West Point</u> (Permit No. WA0022327)

for each plant (identified above) at the following:

Finally, the entire body of effluent monitoring data and reports that are submitted to Ecology as part a DMR package are available on Ecology's "PARIS" database by searching on the Permit No.

#### https://fortress.wa.gov/ecy/paris/PermitLookup.aspx

WTD also conducted additional effluent monitoring during the restoration process for the West Point treatment plant following the February 9, 2017 flooding and damage incident. WTD established a dedicated temporary website to post the collected effluent data, summaries of the data, and other reports and information. With the restoration of the majority of treatment processes and equipment completed in May 2017, and West Point's return to its normal status of routine compliance with permit requirements, the additional monitoring was discontinued and WTD now intends to maintain the temporary website indefinitely until such time it is determined to no longer be necessary. The dedicated website for the environmental monitoring data is:

https://www.kingcounty.gov/depts/dnrp/wtd/system/west/west-point-restoration/environmentalmonitoring.aspx

#### Water Quality Monitoring Data

The County's Water, Resources, and Land Division (WRLD) – Science Section, with assistance from the King County Environmental Laboratory (KCEL), conducts a variety of water quality monitoring programs in the Puget Sound, and the regions rivers and lakes that indirectly contribute to an understanding of the effects of County activities on environmental resources. However, with the exception of limited periodic and specific discharge event conditions, the County is not required under the NPDES permits for the wastewater treatment plants to conduct receiving water quality monitoring at our discharge outfall locations. Consequently, the reader is directed to the WLRD Science Section website where available information on the ambient marine water quality monitoring programs in Puget Sound can be found:

### https://green2.kingcounty.gov/marine

Additionally, WTD in conjunction with WLRD Science Section staff, temporarily expanded and increased the frequency of the routine marine water quality monitoring in Puget Sound at sites near the West Point outfall while the restoration process for the West Point treatment plant was underway following the February 9, 2017 flooding and damage incident. WTD established a dedicated temporary website to post bi-weekly summary reports of Puget Sound water quality conditions during this period, and with West Point's return to a state of compliance with NPDES permit requirements, the additional monitoring was discontinued in June 2017. Furthermore, WTD and WLRD Science Section are involved in conducting supplemental environmental analyses to characterize conditions in Puget Sound resulting from the West Point to determine if any changes in contaminants of concern may have occurred in sediments or marine aquatic organisms. The dedicated website where information from the marine water quality monitoring, and the supplemental sediment and marine organism contaminant investigations, can be found at:

https://www.kingcounty.gov/depts/dnrp/wtd/system/west/west-point-restoration/marinemonitoring.aspx

#### Sediment Monitoring Data

WTD, with assistance from the WLRD Science Section, conducts extensive sediment quality monitoring and analysis for compliance with the NPDES permits for the West Point, South Plant, and Brightwater treatment plants. A large amount of the County's required sediment analysis work is conducted at CSO outfall locations to implement the Post Construction Monitoring Program for the County's 2012 Long-term CSO Control Plan Amendment under the West Point NPDES permit. The CSO program is focused on ensuring that the CSO outfalls meet Washington's sediment quality standards as hydraulic control of each outfall is achieved (i.e., not more than one overflow event per year on a 20-year average). The West Point NPDES permit also requires the County to prepare an update of the 2009 Sediment Data Report by December 1, 2018 to provide a comprehensive summary of information for each CSO outfall and its status with respect to compliance with sediment quality standards. Finally, the County is implementing, and periodically updates, a Sediment Management Program that provides the overarching direction for all of the CSO discharge locations, summarizes ongoing and previously performed sediment cleanup work, summarizes the results of CSO discharge modeling, provides the status of existing sediment quality, and assigns an appropriate sediment management strategy for each CSO. In general, the sediment investigations and development of sediment management strategies at any given CSO outfall is a complex and lengthy process involving multiple actions and participants, and summary information on the status of each project is not readily summarized. Consequently, the reader is directed to the County's dedicated Sediment Management Plan website where available information, reports, news, and status of the program can be obtained:

https://www.kingcounty.gov/services/environment/wastewater/sediment-management/plan.aspx

### March 2020


### 10. Wastewater planned revenue and use of revenue

+

Financial performance (March 2020)

### Wastewater planned revenue and use of revenue

This chart compares WTD planned revenue and use of revenue with monthly actual revenue and use of the revenue collections. Monthly actuals highlight total revenue collected by the sewer rate, capacity charge and other sources, and total use of the revenue collected by operating expenditures, debt service and transfer to capital.

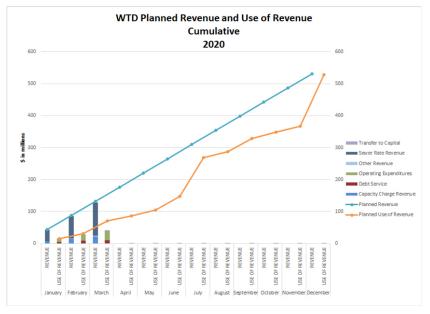

### 11. Cost and schedule of baselined major capital projects

+

### Cost and schedule of baselined major capital projects

This table represents budget and schedule performance of <u>projects with greater than \$1M</u> <u>expected cost  $\beta$ </u>. Performance is measured relative to the baseline point which is established at approximately 30% design completion per established King County Project Management Standards.

| Project<br>Number | Project Name  | Scope Status | Schedule Status | Current<br>Substantial<br>Completion Date | Baseline Duration | <b>Current Duration</b> | Variance at<br>Completion (VAC) | % VAC | Cost Status | Baseline Budget at<br>Completion (BAC) | Current<br>Estimate At<br>Completion (EAC) | Cost Variance<br>At Completion<br>(CVAC) | % CVAC | Report<br>Date |
|-------------------|---|--------------|-----------------|---|-------------------|-------------------------|---------------------------------|-------|-------------|--|--|--|--------|----------------|
| 3611 WAT          | ER QUALITY CONST-UNRES - Wastewater Treat           | ment         |                 |   |                   |                         |                                 |       |             |  |  |  |        |                |
| 1038122           | WTC SUNSET HEATH PS FM UPGRADE                      |              |                 | 9/30/2020                                 | 1,813             | 1,996                   | 183                             | 10 %  |             | \$69,754,491                           | \$75,137,250                               | \$5,382,760                              | 7 %    | Q4 201         |
| 1048077           | WTC ENVIR LAB ENERGY IMPROVMNT                      |              | ۲               | 6/27/2019                                 | 566               | 989                     | 423                             | 74%   | ۲           | \$5,850,874                            | \$8,402,817                                | \$2,551,943                              | 43 %   | Q4 201         |
| 1114382           | WTC NORTH CREEK INTERCEPTOR                         | •            | ۲               | 2/27/2018                                 | 1,604             | 2,052                   | 448                             | 27 %  | ۲           | \$56,590,659                           | \$83,969,562                               | \$27,378,903                             | 48 %   | Q4 201         |
| 1116797           | WTC JAM/ARC BLDG REPLACEMENT                        |              |                 | 5/10/2024                                 | 1,663             | 1,663                   | 0                               | 0%    |             | \$71,290,311                           | \$71,290,311                               | \$0                                      | 0 %    | Q4 201         |
| 1116800           | WTC N MERCER ENATALINT PAR                          |              |                 | 1/11/2024                                 | 2,121             | 2,403                   | 282                             | 13 %  | ۲           | \$116,035,624                          | \$162,192,314                              | \$46,156,690                             | 39 %   | Q4 201         |
| 1116801           | WTC LK HILLS&NW LK SAM INTCPT                       |              | ٠               | 7/18/2024                                 | 1,995             | 2,501                   | 506                             | 25%   |             | \$119,342,432                          | \$119,366,484                              | \$24,052                                 | 0 %    | Q4 201         |
| 1117514           | WTC WEST POINT C-1 RESERVOIR ACCESS                 |              | ٠               | 2/18/2020                                 | 623               | 889                     | 266                             | 42 %  | ۲           | \$1,926,396                            | \$4,036,728                                | \$2,110,332                              | 109 %  | Q4 2019        |
| 1117748           | WTC WP INTERMEDIATE, EPS VFD &<br>DEWATERING ENERGY | •            | ٠               | 7/31/2020                                 | 1,142             | 2,908                   | 1,766                           | 154 % | •           | \$33,541,919                           | \$22,942,804                               | (\$10,599,115)                           | -31 %  | Q4 2019        |
| 1120861           | WTC MOBILE OC UNIT REPLACEMENT                      |              | ٠               | 7/31/2020                                 | 696               | 1,354                   | 658                             | 94%   |             | \$3,171,445                            | \$3,170,886                                | (\$559)                                  | 0 %    | Q4 201         |
| 1121402           | WTC GEORGETOWN WET WEATHER<br>TREATMENT STATION     | •            | •               | 1/23/2022                                 | 2,141             | 2,105                   | -36                             | -1%   | •           | \$260,713,113                          | \$241,495,691                              | (\$19,217,423)                           | -7 %   | Q4 2019        |
| 1121404           | WTC SP RSP MEDIUM VOLT SG REPL                      |              |                 | 11/20/2019                                | 658               | 645                     | -13                             | -1%   | ۲           | \$8,038,164                            | \$7,590,480                                | (\$447,684)                              | -5 %   | Q4 2019        |
| 1123517           | WTC E FLEET MAINT FAC REPLOMNT                      |              | ٠               | 4/10/2021                                 | 750               | 1,642                   | 892                             | 118 % | ۲           | \$9,999,584                            | \$12,815,234                               | \$2,815,650                              | 28 %   | Q4 201         |
| 1123624           | WTC COAL CRK SIPHON TRUNK PARA                      |              | ۲               | 5/29/2026                                 | 2,432             | 2,432                   | 0                               | 0%    | ۲           | \$132,310,569                          | \$132,310,569                              | \$0                                      | 0 %    | Q4 201         |
| 1123626           | WTC SP BIOGAS HEAT SYS IMPROVE                      |              | •               | 5/2/2022                                  | 1,410             | 1,847                   | 437                             | 30 %  |             | \$59,897,304                           | \$52,293,228                               | (\$7,604,076)                            | -12 %  | Q4 201         |
| 1123627           | WTC WP 2ND MIX LIQ BLOWER REPL                      |              |                 | 2/5/2021                                  | 640               | 640                     | 0                               | 0%    | ۲           | \$3,994,447                            | \$3,994,447                                | \$0                                      | 0 %    | Q4 201         |
| 1123630           | WTC ESI SECT 2 REHAB PHASE II                       |              |                 | 3/27/2020                                 | 521               | 578                     | 57                              | 10 %  |             | \$45,812,381                           | \$30,055,210                               | (\$15,757,171)                           | -34 %  | Q4 201         |
| 1125460           | WTC BW FF LINKING DEVICE UPGRD                      |              | ٠               | 10/1/2019                                 | 466               | 680                     | 214                             | 45%   |             | \$1,203,778                            | \$1,345,950                                | \$142,172                                | 11 %   | Q4 201         |
| 1127059           | WTC WP REPLC INCINERATOR FLARE                      |              | •               | 4/13/2019                                 | 559               | 879                     | 320                             | 57 %  |             | \$4,825,164                            | \$4,787,062                                | (\$38,102)                               | 0 %    | Q4 201         |
| 1127489           | WP PRIMARY SED ROOF STRUCTURE                       |              |                 | 10/27/2022                                | 1,387             | 1,387                   | 0                               | 0%    |             | \$37,658,373                           | \$37,658,373                               | \$0                                      | 0 %    | Q4 201         |
| 1127842           | WTC INSTALL LK HILLS GENERATOR                      | ۲            | ۲               | 9/2/2022                                  | 1,064             | 945                     | -119                            | -11 % | ۲           | \$5,386,868                            | \$5,386,868                                | \$0                                      | 0 %    | Q4 201         |
| 1128127           | WTC WP DRY POLYMER FEEDER REPL                      |              | ٠               | 6/7/2019                                  | 453               | 865                     | 412                             | 90 %  | ٠           | \$1,100,769                            | \$1,555,559                                | \$454,790                                | 41 %   | Q4 2019        |
| 1129093           | WTC HENDERSON/MLK JR WWTS<br>IMPROVEMENTS           |              | ٠               | 9/19/2019                                 | 391               | 800                     | 409                             | 104 % | ٠           | \$1,810,658                            | \$2,620,953                                | \$810,296                                | 44 %   | Q4 2019        |
| 1129526           | WTC WP LSG PIPING REPLACEMENT                       |              |                 | 12/31/2026                                | 2,634             | 2,634                   | 0                               | 0%    |             | \$24,920,340                           | \$24,920,340                               | \$0                                      | 0 %    | Q4 2019        |

#### Q4 2019 Baseline Report

### March 2020

+

| - <b>-</b>        | Agency: Wattewater Treatment, Fund. All, Year. 2020, Qtr. 1 at Quarter, Cost Status: All, Schedule Status: All, Scope Status: All, Project: A |              |                 |   |                   |                  |                                 |       |             |  |  |  |        |                |
|-------------------|---|--------------|-----------------|---|-------------------|------------------|---------------------------------|-------|-------------|--|--|--|--------|----------------|
| Project<br>Number | Project Name  | Scope Status | Schedule Status | Current<br>Substantial<br>Completion Date | Baseline Duration | Current Duration | Variance at<br>Completion (VAC) | % VAC | Cost Status | Baseline Budget at<br>Completion (BAC) | Current<br>Estimate At<br>Completion (EAC) | Cost Variance<br>At Completion<br>(CVAC) | % CVAC | Report<br>Date |
| 3611 WAT          | ER QUALITY CONST-UNRES - Wastewater Treat   | nent         |                 |   |                   |                  |                                 |       |             |  |  |  |        |                |
| 1130937           | WTC DRAWING DOCUMENT CONTROL  |              | •               | 5/15/2020                                 | 198               | 318              | 120                             | 60 %  | ۰           | \$1,641,376                            | \$1,640,476                                | (\$900)                                  | 0 %    | Q1 2020        |
| 1131919           | WTC BW MEMBRANE FEED PUMP VFD   |              |                 | 11/13/2019                                | 617               | 618              | 1                               | 0%    | ۲           | \$1,765,063                            | \$1,764,743                                | (\$320)                                  | 0%     | Q1 2020        |
| 1134071           | WTC OVATION CONT SYS UPGD   |              |                 | 12/31/2021                                | 975               | 975              | 0                               | 0%    | ٠           | \$15,547,968                           | \$15,547,968                               | \$0                                      | 0 %    | Q1 2020        |
| 1134073           | WTC VFD REPLACEMENT   |              |                 | 9/25/2024                                 | 1,695             | 1,695            | 0                               | 0%    |             | \$12,104,063                           | \$12,104,063                               | \$0                                      | 0 %    | Q1 2020        |
| 1134166           | Conveyance Station Operational<br>Improvements  | •            | ٠               | 6/19/2020                                 | 168               | 248              | 80                              | 47 %  | •           | \$1,357,025                            | \$1,224,151                                | (\$132,874)                              | -9 %   | Q1 2020        |
| 1134301           | WTC PIMS REPLACEMENT  | •            | ٠               | 10/18/2020                                | 371               | 474              | 103                             | 27 %  | ۲           | \$1,844,892                            | \$1,844,264                                | (\$627)                                  | 0 %    | Q1 2020        |
| 1134813           | WTC SP ODOR MOD AT DAFT AREAS   | ۲            |                 | 6/17/2021                                 | 639               | 639              | 0                               | 0%    | ۲           | \$2,655,636                            | \$2,646,566                                | (\$9,071)                                | 0 %    | Q1 2020        |
| 1136153           | WTC WPTP C-1 RESERVOIR ACCESS   |              | ٠               | 3/27/2020                                 | 623               | 927              | 304                             | 48 %  | ٠           | \$1,926,397                            | \$3,815,306                                | \$1,888,909                              | 98 %   | Q1 2020        |
| 1136470           | WTC LOOP BIOSOLDS COMP PLT SP   | ٠            | ٠               | 6/21/2022                                 | 657               | 917              | 260                             | 39 %  | ٠           | \$3,325,571                            | \$3,325,571                                | \$0                                      | 0 %    | Q1 2020        |
| 1136471           | WTC DECOMISSION SP FUEL CELPP   |              |                 | 2/4/2021                                  | 352               | 352              | 0                               | 0%    |             | \$1,323,892                            | \$1,323,892                                | \$0                                      | 0 %    | Q1 2020        |
| 1136747           | WTC PS LEVEL CONTROL IMPROVE  |              | ٠               | 6/30/2020                                 | 269               | 329              | 60                              | 22 %  | ٠           | \$1,590,170                            | \$1,588,259                                | (\$1,911)                                | 0 %    | Q1 2020        |
| 3612 WTD          | 612 WTD INTERNALLY FINANCED PROJECTSS - Wastewater Treatment  |              |                 |   |                   |                  |                                 |       |             |  |  |  |        |                |
| 1134078           | WTC BW MBR LEAP UPGD  |              |                 | 8/30/2019                                 | 293               | 262              | -31                             | -10 % | •           | \$2,459,396                            | \$1,561,501                                | (\$897,895)                              | -36 %  | Q1 2020        |

| on: 04/28/2020 12:06 | Status Legend: 🔵 Green | 🔺 Yellow | 🔶 Red | Gray (no info) | Page 2 of 2 |
|----------------------|------------------------|----------|-------|----------------|-------------|
|                      |                        |          |       |                |             |

### Safety performance (March 2020)

### 12. WTD accident (claim) summary


### WTD accident (claim) summary

Created on

Q1 2020 Baseline Report

The following summary graphs illustrate employee accident and job injury claim experience (for current month and year to date) for the Wastewater Treatment Division.

WTD Claims Summary 🖄 (February 2020)

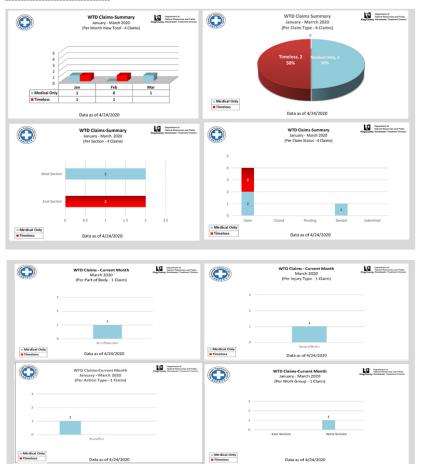

| Ma | rch | 2 | 02 | 0 |
|----|-----|---|----|---|
|----|-----|---|----|---|

+

+

+

÷

|                            | WTD Claims - Current Month<br>March 2020<br>(Per Job Title - 1 Claim) | Department of<br>Notes Reserves and Parks<br>Reg Covery Restances Produced Disaster |  | WTD Claims - Current Month<br>March 2020<br>(Per Time - 1 Claim)   | King County Worksouth of<br>Rang County Worksouth Theorem and Parks |
|----------------------------|---|---|--|--|---|
| ind Maint Mech/Lead/Master | 1   |   | 2<br>1<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0<br>0 | 4 (1992)<br>4 (199 | 103-359<br>402-459<br>ne record                                     |
| Medical Only Timeloss      | 0 1 2<br>Data as of 4/24/2020   | 3   | Medical Only Timeloss  | · 이 의 의 의 의 의 의 의 의 의 의 의 의 의 의 의 의 의 의  | No ti   |

- The term Medical Only Claim refers to employee accident that requires attention from a healthcare provider. The injured worker may be released completely after treatment or released with work restrictions requiring work accommodation.
- The term Timeloss Claim refers to claims that are serious enough to warrant the doctor taking the injured worker off his regular duty for a period of time. The injured worker may be released to modified (light) duty during his recovery period. As long as the employer accommodates the doctor's restrictions on the injured worker's activity during the light duty period, the claim may remain as medical only - if the injured worker returns to light duty before the elimination period lapses.

### Monthly archives

Past performance metrics are posted by month in portable document format 🖄.

### <u>2020</u>

- February 2020
- January 2020

### <u>2019</u>

- December 2019
- November 2019
- October 2019
- September 2019
- August 2019
- July 2019
- June 2019
- <u>May 2019</u>
- April 2019
- March 2019
- <u>February 2019</u>
- January 2019

### <u>2018</u>

- December 2018
- November 2018
- October 2018
- September 2018
- <u>August 2018</u>
- July 2018
- June 2018
- May 2018
- April 2018
- March 2018
- February 2018
- January 2018

### <u>2017</u>

- December 2017
- November 2017
- October 2017
- September 2017
- <u>August 2017</u>
- July 2017

### March 2020

| Wastewater | Treatment |
|------------|-----------|
| Division   |           |

King Street Center 201 S. Jackson St., Suite 500 Seattle, WA 98104







Last Updated September 30, 2019
